1st and final B:4

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work:— Improvement to Bo cc Road and drain Kogilu main Road to Anjeneya temple road in Kempegowda ward ward						
	Job code:- 001-19-000058.						
	H/A:- PITTI. Zone works pwd works.						
	A/S :- CE/NRS/A.S/191/2018-19 dt 25-02-2019						
	T/S :- EE/YNRD/TS/32/2018-19 dt 25-02-2019						
	Work estn :- EE(YNRD) E-PMT/09-00155/2019-20 dt 05-07-2019						
	Agency :- Sri Vinayak. K. R. No-42 4th main Road Bhuvaneshwari Nagar Bangalore						

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

116818

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work..... pre measurement recorded.

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
1)	Earthwork excavation for foundation of building walls, supply, sanitary line and Electrical conduits either in pits or in trenches 1.50 mt above in widths in ordinary soil not exceeding 1.50 m in depth including dressing the bottom & sides of pits and trenches stacking the excavated soil clear from edges of excavation with lead up to 50 m after breaking of clods complete as per Spm Dhonakaya Road. From NH 7 towards Kagiliu main Road. Start From NH 7 Service Road. Bell mouth portion 1		12.10	$\frac{(5.50+4.10+3.35)}{3}$	0.75	= 14.25 m^3	

pre measurement recorded.

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	haulage and return trip complete as per Item. as vide item 100-01.						
	Qty - 233.48 m^3 @ 478-31/m^3						Rs-18284-00
						Total Amount	1195050-00
						Add 12% G.ST.	0143405-00
						Total Rs	1338456-00

Executive Engineer
Yelahanka Sub. Division
(BBMP Yrk. Zn)
Yelahanka, Bangalore

Scanned by CamScanner

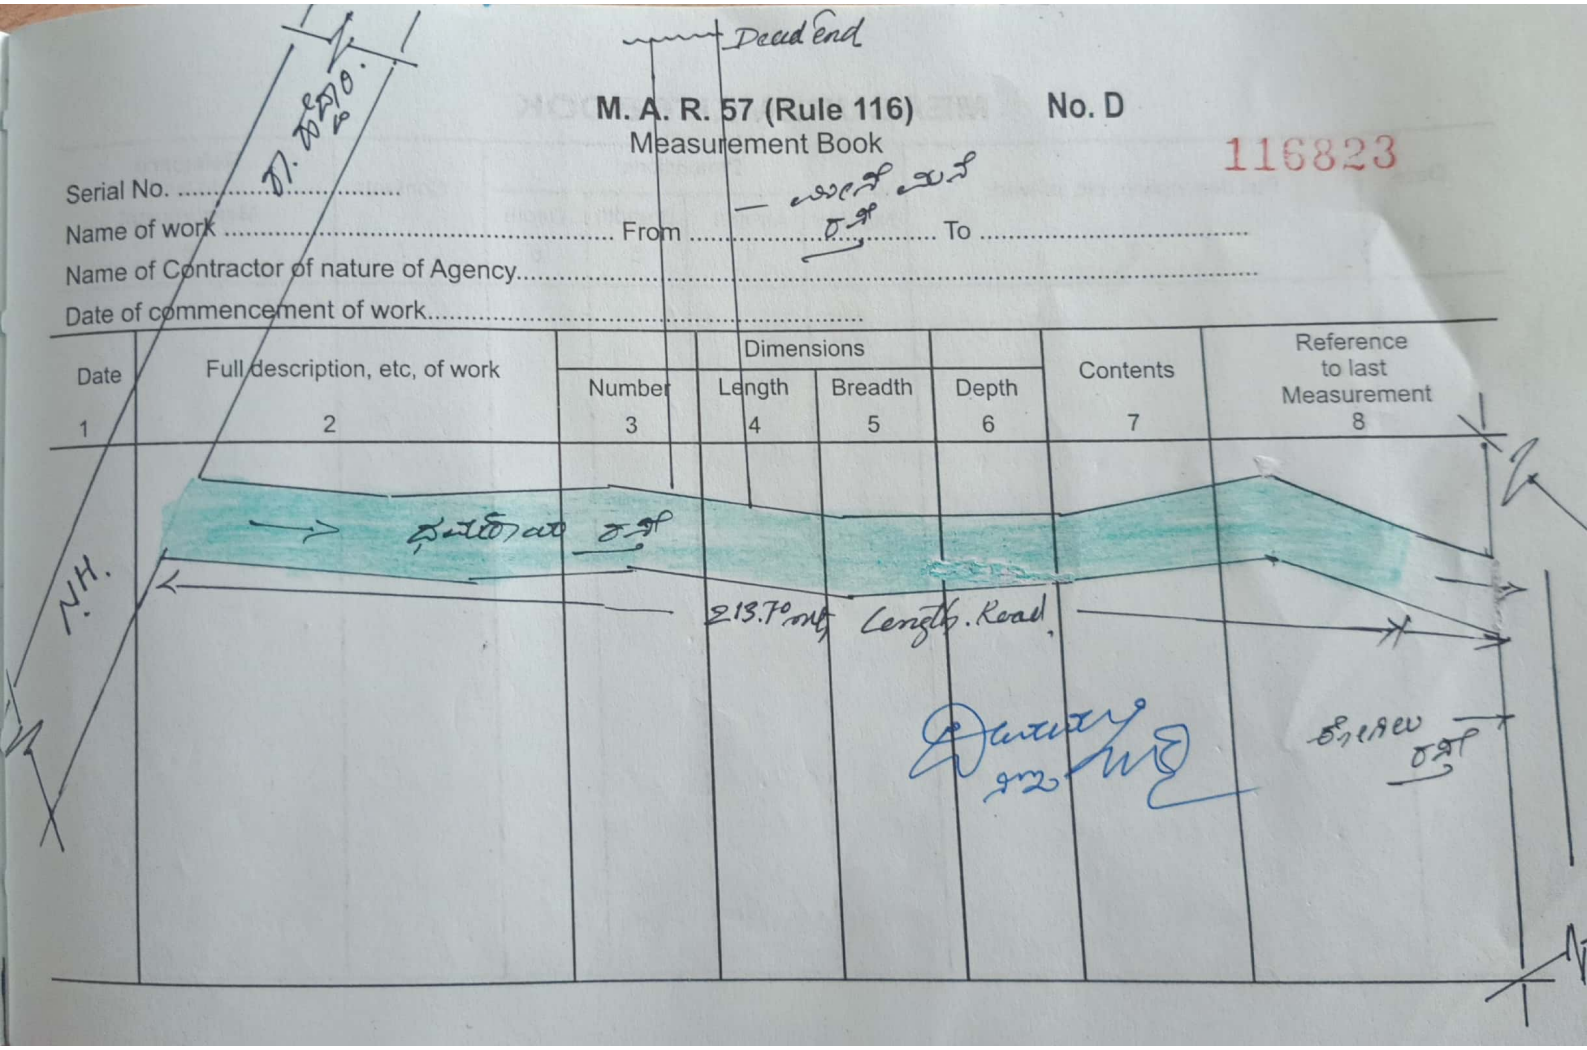

Scanned by CamScanner
